


Ashiana Tarang Phase VII

Phase Start

01 June 2026

Sr.No	Description	Start Date	Duration	Finish Date
1	Foundation	01-Jun-26	90	30-Aug-26
2	RCC super structure	31-Aug-26	390	28-Apr-27
3	Brick Work	02-Dec-26	350	17-Nov-27
4	Internal Plaster	31-Jan-27	350	16-Jan-28
5	Tiles Work	01-Apr-27	350	16-Mar-28
6	External Plaster	06-Apr-27	300	31-Jan-28
7	POP Work	05-Jun-27	300	31-Mar-28
8	Door Shutter Fixing	04-Aug-27	300	30-May-28
9	Aluminium Window	04-Aug-27	300	30-May-28
10	Electrical wiring & Fittings and testing	26-Aug-27	305	26-Jun-28
11	Internal Painting	25-Oct-27	300	20-Aug-28
12	CP & Vitreous Fittings	22-Apr-28	350	07-Apr-29
13	External Painting	23-Jan-28	300	18-Nov-28
14	Fire Fighting	02-Nov-27	300	28-Aug-28
15	Lift	24-Nov-27	300	19-Sep-28
16	Solar	12-May-28	290	26-Feb-29
17	Filling and Obtaining Completion Certificate	01-Apr-29	30	30-Apr-29
18	Final finishing and hand over	15-Feb-29	350	31-Jan-30

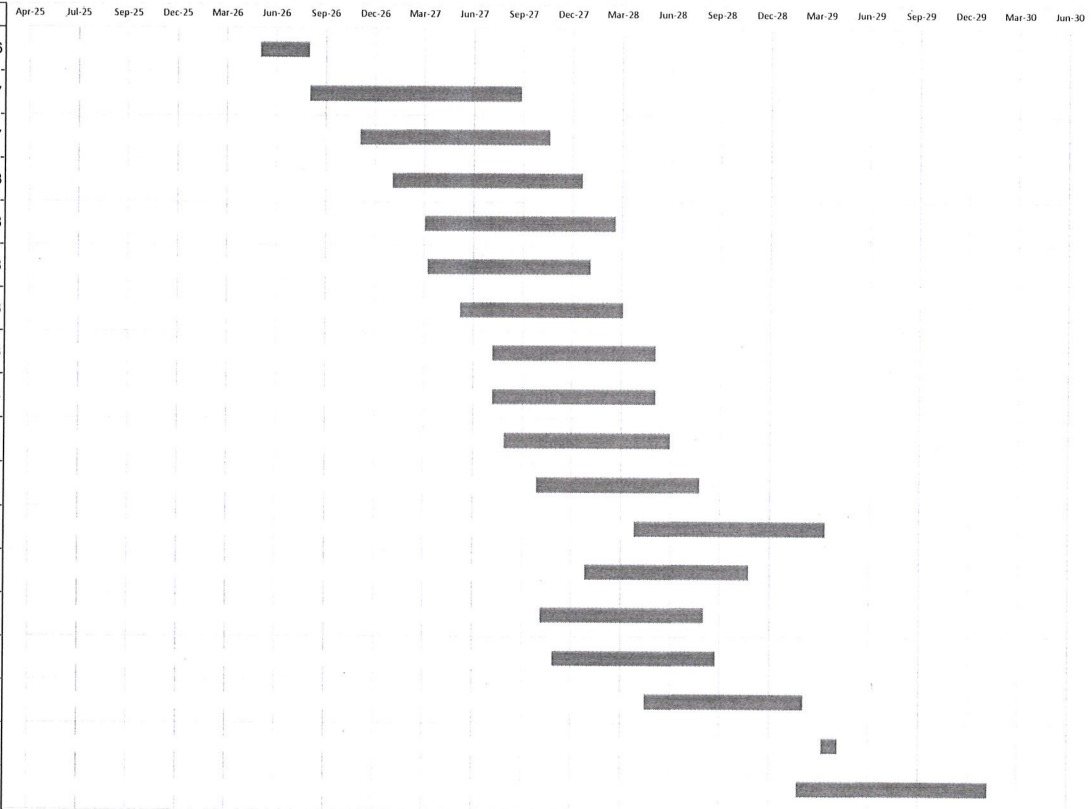

For Ashiana Housing Limited

[Signature]

Authorised Signatory
