


Ashiana Aravali

Phase Start Date = 01 September 2025

Sr.No	Description	Start Date	Duration	Finish Date
1	Foundation	02-Dec-25	150	01-May-26
2	RCC super structure	02-May-26	250	07-Jan-27
3	Brick Work	03-Aug-26	302	01-Jun-27
4	Internal Plaster	02-Oct-26	303	01-Aug-27
5	Tiles Work	01-Dec-26	302	29-Sep-27
6	External Plaster	06-Dec-26	300	02-Oct-27
7	POP Work	04-Feb-27	300	01-Dec-27
8	Door Shutter Fixing	07-Mar-27	300	01-Jan-28
9	Aluminium Window	05-Apr-27	300	30-Jan-28
10	Electrical wiring & Fittings and testing	07-Apr-27	305	06-Feb-28
11	Internal Painting	07-May-27	300	02-Mar-28
12	CP & Vitreous Fittings	10-Aug-27	250	16-Apr-28
13	External Painting	06-Jul-27	250	12-Mar-28
14	Fire Fighting	20-May-27	240	15-Jan-28
15	Lift	18-Mar-27	300	12-Jan-28
16	Solar	04-Sep-27	178	29-Feb-28
17	Final finishing and hand over	16-Apr-28	137	31-Aug-28

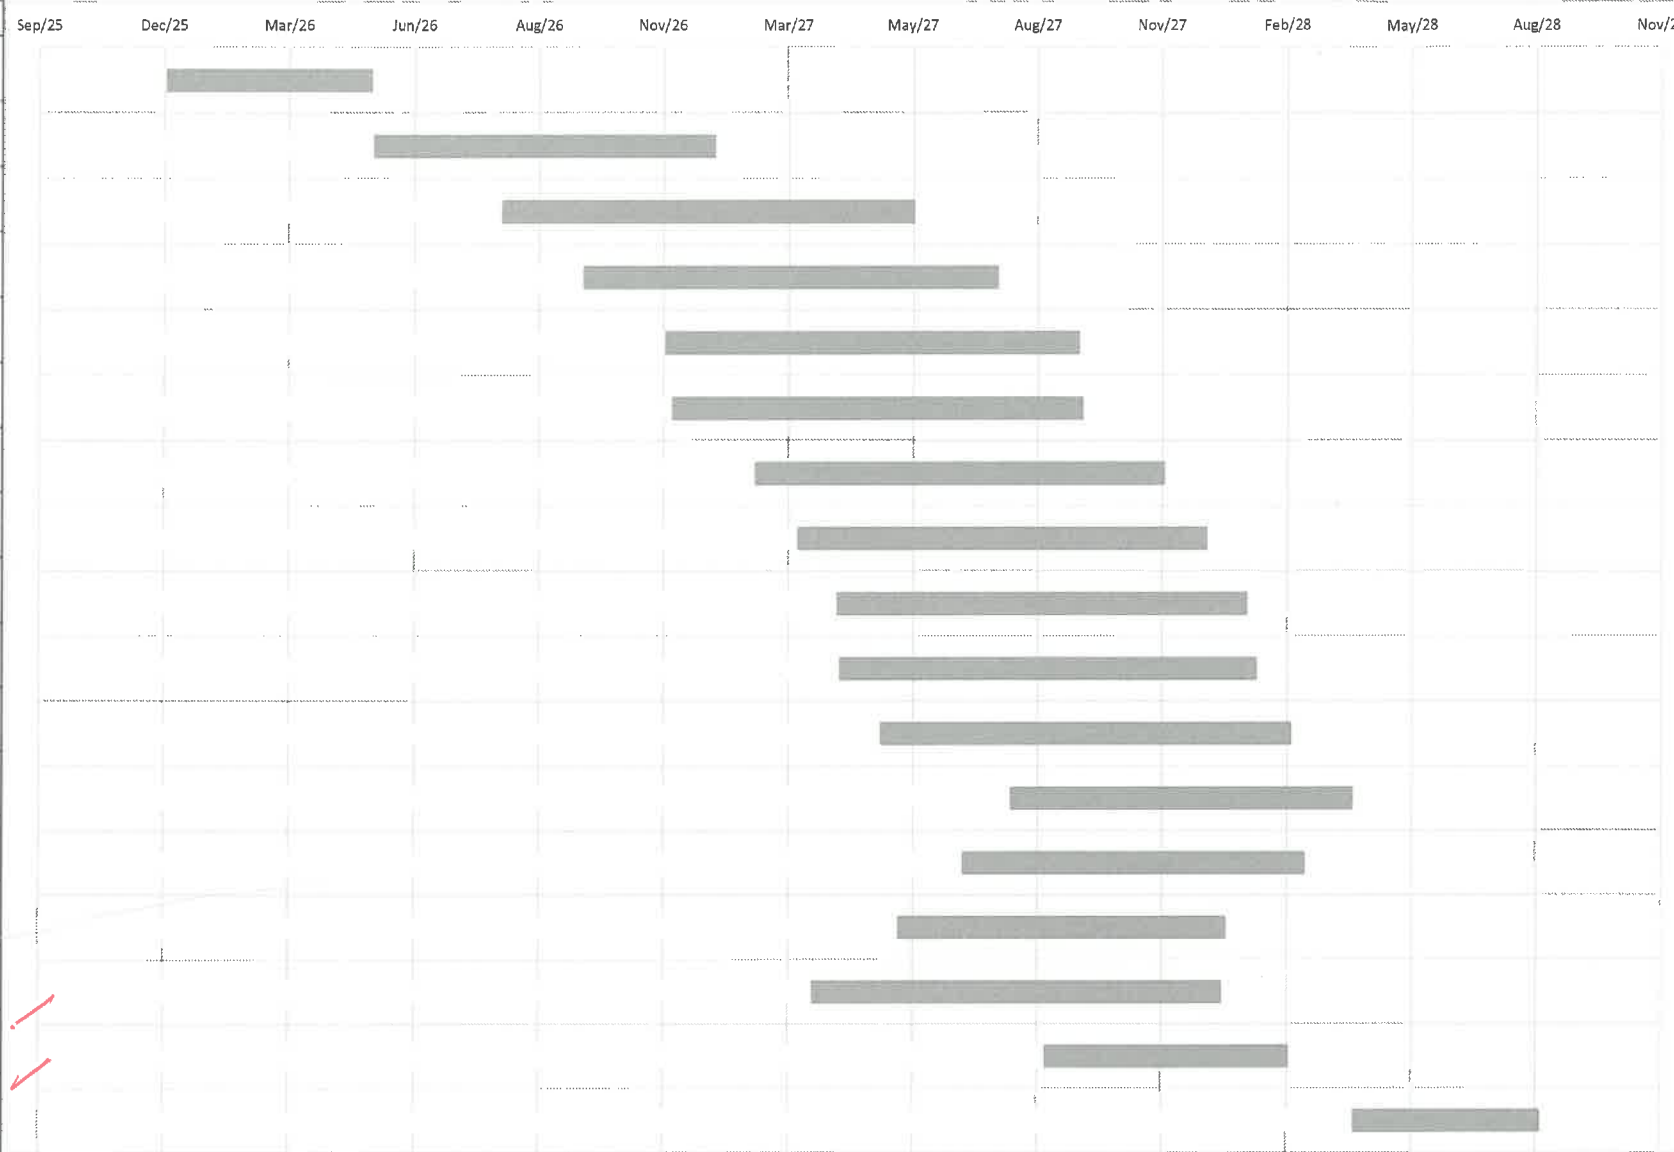

7/3/2025
